

Coring Report

Parkwood Dr. & Kerry Ln Waterline & Pavement Improvements

PREPARED FOR
City of Wickliffe

Verdantas Project No. 32252
August 25, 2025





Pavement Coring Report

Project Name: 2025 Road Improvements

Project Number: 250262

Project Owner: City of Wickliffe

Location: Kerry Lane

Prime Contractor: ----

Paving Contractor: ----

Core Diameter: 4"

Type: Thickness ____ Exploratory X

Date: 12/10/24

Technician: Wm Barson

Core #	Location	Cored Material Description	Actual Material Thickness In Inches	Plan Depth	Condition/Type of Subgrade -Aggregate Size -Remarks
1	30564 Kerry Lane south side of road 15' east of M/B 3.5' south of C/L	Asphalt	1.5	N/A	1/2" max aggregate - limestone & bank gravel
		Asphalt	1.0	N/A	1" max aggregate limestone & slag
		Asphalt	1.8	N/A	1/2" max aggregate - limestone & slag
		Asphalt	2.0	N/A	1" max aggregate limestone & slag
		Concrete	UNK	N/A	
					Partial depth core only. Unknown base/sub-base material.
		Sub-total cored	6.3		
2	30555 Kerry Lane north side of road 5.75' from curb	Asphalt	1.5	N/A	1/2" max aggregate - limestone & bank gravel
		Asphalt	1.5	N/A	1/2" max aggregate limestone
		Asphalt	2.0	N/A	3/4" max aggregate - limestone & slag
		Concrete	2.5	N/A	1" max aggregate slag
					Base material: brown sand and stone
		Sub-total cored	7.5		



Pavement Coring Report

Project Name: Parkwood Dr & Kerry Ln Waterline Improvements
Project Number: 32252 **Prime Contractor:** ----
Project Owner: City of Wickliffe **Paving Contractor:** ----
Location: Parkview Rd & Kerry Ln **Core Diameter:** 4"
Type: Thickness ___ Exploratory X
Date: 08/25/25 **Technician:** Owen Kaufman

Core #	Location	Cored Material Description	Actual Material Thickness In Inches	Plan Depth	Condition/Type of Subgrade -Aggregate Size -Remarks
3	30555 Kerry Ln see attached map 4' from face of curb east side of road.	Asphalt	2.0	N/A	3/4" max aggregate - limestone and bank gravel
		Asphalt	2.0	"	1/2" max aggregate - limestone, bank gravel, and slag
		Concrete	4.0	"	1" max aggregate - limestone
		Sub-total cored	8.0		
4	30571 Kerry Ln. see attached map 17'6" from face of curb on west side of cul-de-sac.	Asphalt	2.0	N/A	1/2" max aggregate - limestone & bank gravel
		Asphalt	3.0	"	3/4" max aggregate - limestone, bank gravel, & slag
		Sub-total cored	5.0		
5	29474 Parkwood Dr see attached map 10'6" from face of curb on west side of road.	Asphalt	1.3	N/A	1/2" max aggregate - limestone & bank gravel
		Asphalt	2.8	"	1/2" max aggregate - limestone & bank gravel
		Concrete	5.0	"	2" max aggregate - limestone
		Sub-total cored	9.0		
		Total Cored	22.0		



Pavement Coring Report

Project Name: Parkwood Dr & Kerry Ln Waterline Improvements

Project Number: 32252

Prime Contractor: ----

Project Owner: City of Wickliffe

Paving Contractor: ----

Location: Parkview Rd & Kerry Ln

Core Diameter: 4"

Type: Thickness ___ Exploratory X

Date: 08/25/25

Technician: Owen Kaufman

Core #	Location	Cored Material Description	Actual Material Thickness In Inches	Plan Depth	Condition/Type of Subgrade -Aggregate Size -Remarks
6	29481 Parkwood Dr. see attached map 3'9" from face of curb on west side of road.	Asphalt	1.5	N/A	3/4" max aggregate - limestone
		Asphalt	1.5	"	1/2" max aggregate - limestone & bank gravel
		Concrete	8.0	"	1-1/2" max aggregate - limestone
					Base is concrete pavement.
		Sub-total cored	11.0		
7	see attached map 3'9" from face of curb on east side of road.	Asphalt	1.8	N/A	1/2" max aggregate - limestone & bank gravel
		Asphalt	3.5	"	1" max aggregate - limestone & bank gravel
					Base is concrete pavement.
		Sub-total cored	5.3		

Pavement Coring Report

Project Name: 2025 Road Improvements

Project Number: 250262

Project Owner: City of Wickliffe

Location: Kerry Lane

Date: 12/10/24

Prime Contractor: ---

Paving Contractor: ---

Core Diameter: 4"

Type: Thickness ___ Exploratory X

Technician: Wm Barson

CORE #1



CORE LOCATION



CORE OPENING



CORE SAMPLE

Pavement Coring Report

Project Name: 2025 Road Improvements

Project Number: 250262

Project Owner: City of Wickliffe

Location: Kerry Lane

Date: 12/10/24

Prime Contractor: ----

Paving Contractor: ----

Core Diameter: 4"

Type: Thickness ____ Exploratory X

Technician: Wm Barson

CORE #2



CORE LOCATION



CORE OPENING



CORE SAMPLE



BASE MATERIAL

Pavement Coring Report

Project Name: Parkwood Dr & Kerry Ln Waterline Improvements

Project Number: 32252

Project Owner: City of Wickliffe

Location: Parkview Rd & Kerry Ln

Prime Contractor: ----

Paving Contractor: ----

Core Diameter: 4"

Type: Thickness ___ Exploratory X

Date: 08/25/25

Technician: Owen Kaufman

CORE #3



CORE LOCATION



CORE OPENING



CORE SAMPLE

Pavement Coring Report

Project Name: Parkwood Dr & Kerry Ln Waterline Improvements

Project Number: 32252

Project Owner: City of Wickliffe

Location: Parkview Rd & Kerry Ln

Prime Contractor: ----

Paving Contractor: ----

Core Diameter: 4"

Type: Thickness Exploratory X

Date: 08/25/25

Technician: Owen Kaufman

CORE #4



CORE LOCATION



CORE OPENING



CORE SAMPLE

Pavement Coring Report

Project Name: Parkwood Dr & Kerry Ln Waterline Improvements

Project Number: 32252

Project Owner: City of Wickliffe

Location: Parkview Rd & Kerry Ln

Prime Contractor: ----

Paving Contractor: ----

Core Diameter: 4"

Type: Thickness Exploratory X

Date: 08/25/25

Technician: Scott Pirc

CORE #5



CORE LOCATION



CORE OPENING



CORE SAMPLE

Pavement Coring Report

Project Name: Parkwood Dr & Kerry Ln Waterline Improvements

Project Number: 32252

Project Owner: City of Wickliffe

Location: Parkview Rd & Kerry Ln

Prime Contractor: ----

Paving Contractor: ----

Core Diameter: 4"

Type: Thickness ___ Exploratory X

Date: 08/25/25

Technician: Owen Kaufman

CORE #6



CORE LOCATION



CORE OPENING



CORE SAMPLE

Pavement Coring Report

Project Name: Parkwood Dr & Kerry Ln Waterline Improvements

Project Number: 32252

Project Owner: City of Wickliffe

Location: Parkview Rd & Kerry Ln

Prime Contractor: ----

Paving Contractor: ----


Core Diameter: 4"

Type: Thickness ___ Exploratory X

Date: 08/25/25

Technician: Owen Kaufman


CORE #7

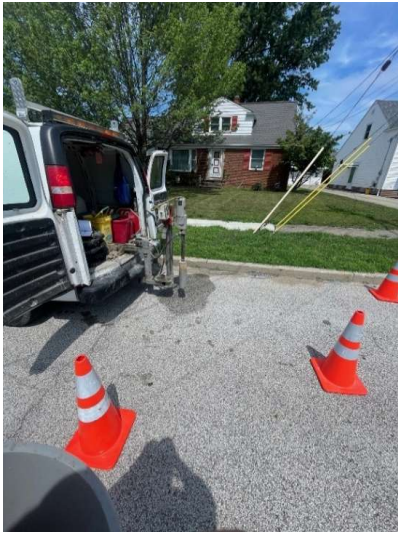



CORE LOCATION



CORE OPENING

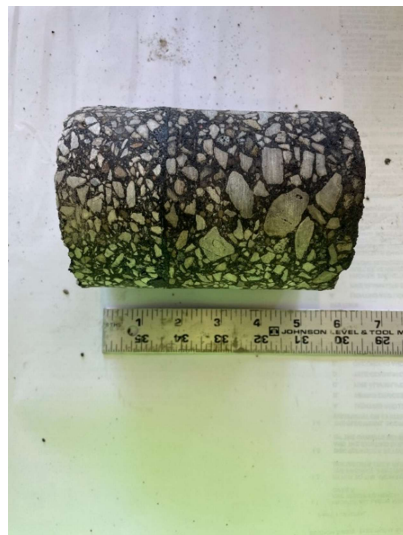

CORE SAMPLE

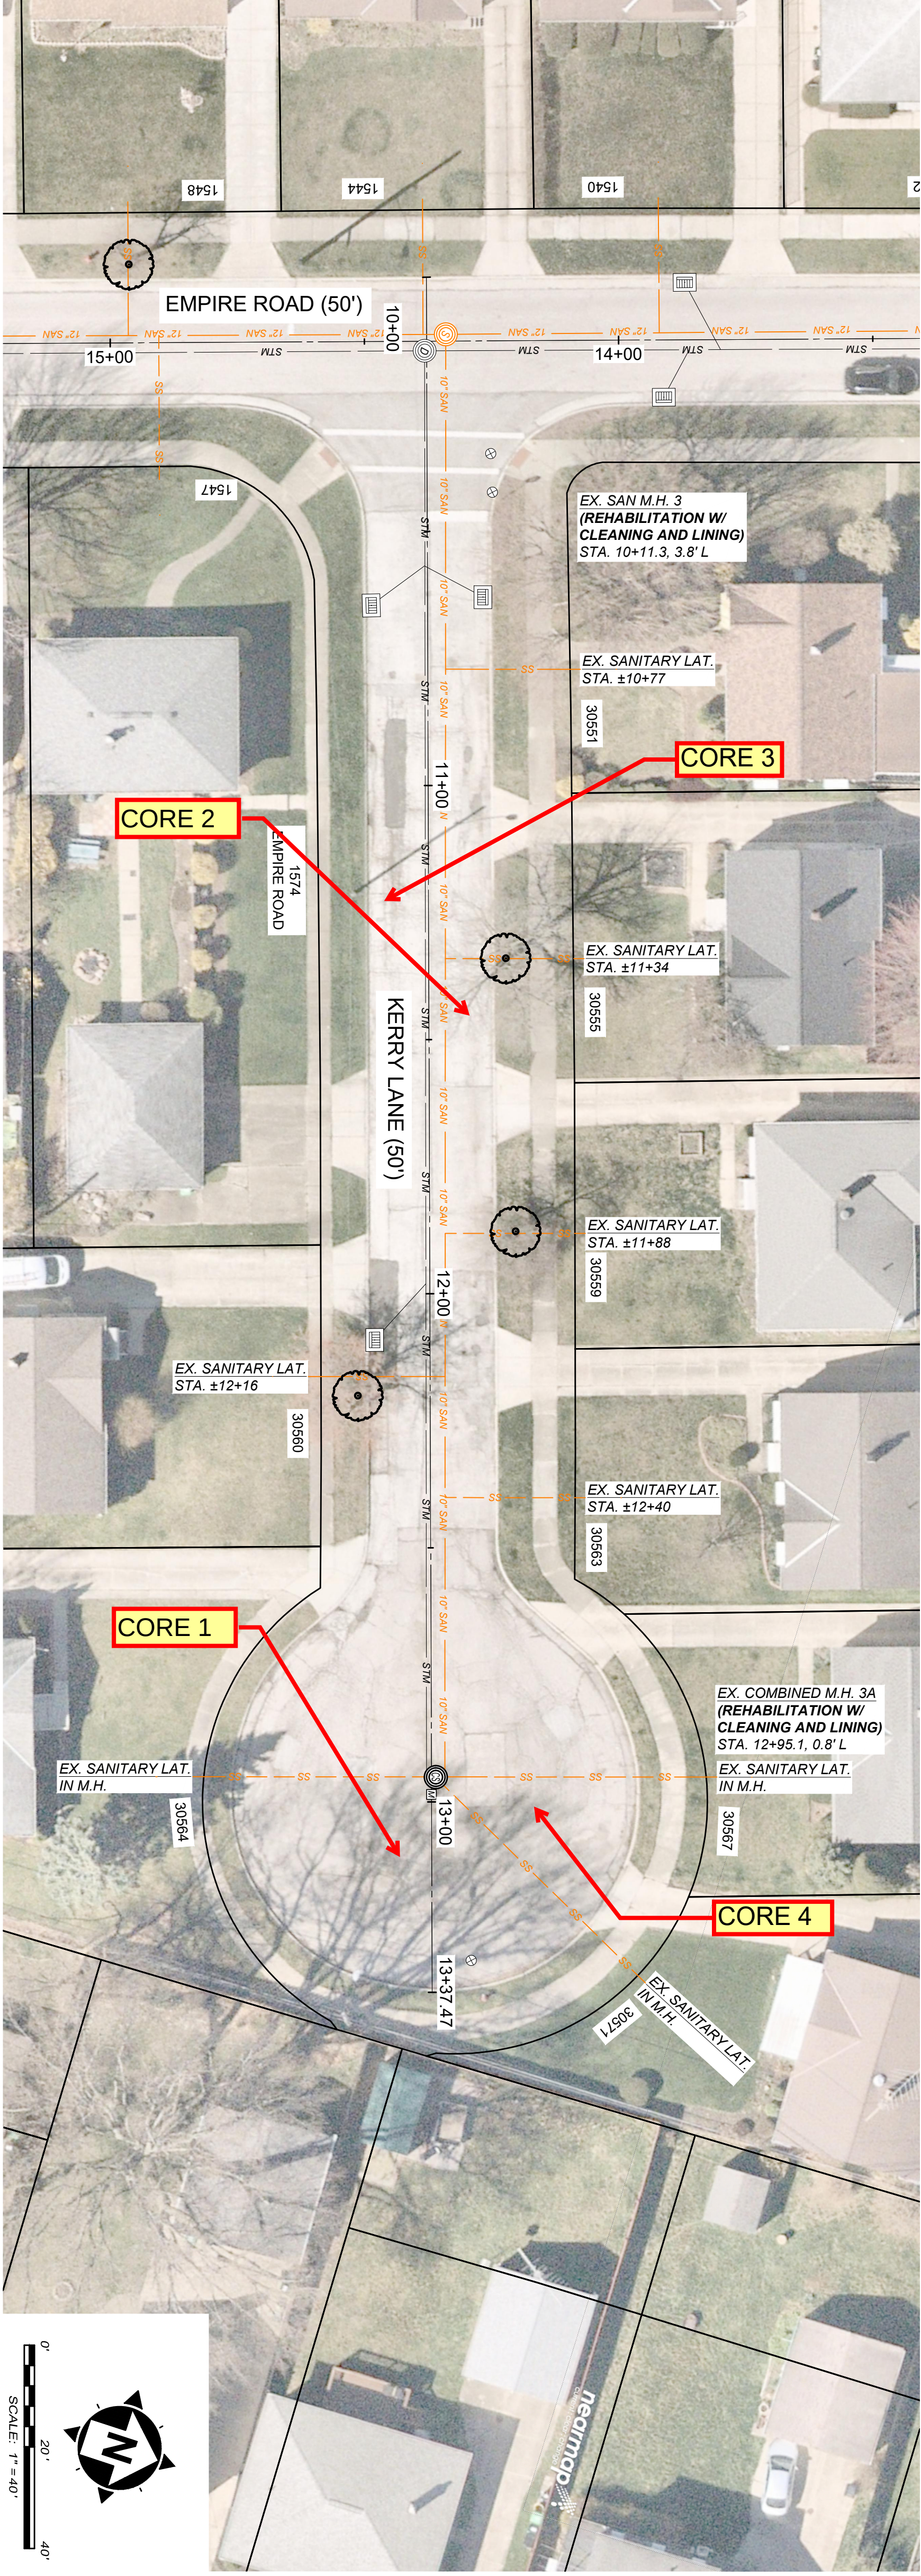

0'
20'
40'
SCALE: 1" = 40'

